


N.E.B. COPY

PARA ET AL FORT LIARD



Drill Stem Test Report


Prepared for: PARAMOUNT RESOURCES
4700, 888 - 3rd Street S.W.
CALGARY, AB

Well Name: PARA ET AL FORT LIARD
Location: N-01-60-10-123-15

Test Date: 01/12/2001

Job Ticket #: D2-8621 DST#: 8

N-01-60-10-123-15



DST #8



Drill Stem Testing Report

Company: PARAMOUNT RESOURCES LTD.
4700, 888 - 3rd Street S.W.
CALGARY, AB

Job Ticket #: D2-8621 DST#: 8
Test Date: 01/12/2001 939hrs

Well Name: PARA ET AL FORT LIARD

Contact: WILBERT CALLIHO

Location: N-01-60-10-123-15

General Information:

Test Type: INFLATE STRADDLE
Interval: 1368.00m - 1379.00m
Formation: BELLOY
KB Elevation: 492.10m
Ground Elevation: 487.00m
Total Depth: 1940.00m
Test Mode: Fluid

Tester: D. WHITE
Truck No.: Unit 677
Contractor: PRECISION
Rig No.: 387
Hole Diameter: 222mm
Hole Condition: GOOD
Bottom Hole Temperature: 49.80 C

Electronic Recorder Information:

OUTSIDE
Recorder #: 124

Range: 70000 kPa
Depth: 1370.92 m

FLUID
Recorder #: 126

Range: 70000 kPa
Depth: 1347.09 m

Flag Points:

Flag Points:	Time:	Pressure:
A Initial Hydrostatic	0.00	16539.5
B Start of 1st Flow	0.00	408.3
C End of 1st Flow	8.00	428.2
D End of 1st Shutin	65.00	6292.9
E Start of 2nd Flow	0.00	253.5
F End of 2nd Flow	30.00	490.7
G End of 2nd Shutin	191.00	8509.4
Q Final Hydrostatic	0.00	16197.0

Test Run Information:

Start Time: 939hrs
Reached Test Depth: 1500hrs
Pull Out Time: 2030hrs
Tool Out Of Hole: 100hrs

Weight set on Packers: 6000.00daN
Weight to free Packers: 10000.00daN
Initial String Weight: 39000.00daN
Unseated String Weight: 39000.00daN

Tool Chased Dist: 0.00m
Mud Type: GEL CHEMICAL
Mud Weight: 1190.00kg/m³
Amount of fill: 0.00m
Amt of cushion: 0.00
Type of cushion:

Water Loss: 6.50cm³
Mud Drop: NO
VIS: 95.00S/L
Filter Cake: 2.00mm
Pump Time: 30min
Reversed Out: NO

General Remarks:

Mechanically successful. *Test results suggest low permeability within the zone tested.

PREFLOW: Strong air blow throughout.


FINAL FLOW: Strong air blow throughout. Gas to surface in 2 minutes, lazy 2 meter flare decreasing to 1/2 meter after 30 minutes. Rates too small to measure.

Recovery Description:

Total fluid recovery was 35 meters of drilling fluid.

Gas to surface.

Gas Bomb: 1 Sampler: 1
Fluid Sample: 3 Sent to: AGAT LAB

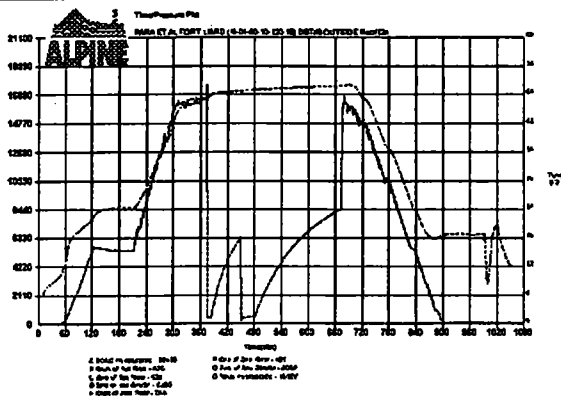



Drill Stem Testing - Tool Diagram / Description

Company: PARAMOUNT RESOURCES LTD.
4700, 888 - 3rd Street S.W.
CALGARY, AB

Job Ticket #: D2-8621 DST#: 8
Test Date: 01/12/2001 939hrs

Well Name: PARA ET AL FORT LIARD

Contact: WILBERT CALLIHOO

Location: N-01-60-10-123-15

Inflate Straddle

Drill Collar Stands:	3
Drill Collar Singles:	0
Drill Pipe Stands:	68
Drill Pipe Singles:	1
Heavy Wt. Pipe Stands:	20
Heavy Wt. Pipe Singles:	0
Total Drill Collars/Pipe and Tools:	1370.67m
Total Drill Pipe Above K.B.:	2.67m
Total Depth:	1940m

Tool / Drill Stem Information:

Tool Weight:	2000.00	daN
Drill Collar Inside Diameter:	54.00	mm
Drill Collar Length:	54.49	m
Drill Pipe Inside Diameter:	97.00	mm
Drill Pipe Length:	920.42	m
Heavy Weight Pipe Diameter:	69.00	mm
Heavy Weight Pipe Length:	372.42	m
Bottom Choke Diameter:	12.70	mm
Number of Packers: 2 Dia.:	196.90	mm

23.34m

38.85m

Tool Remarks:

Depth:
1368m


10.94m

Depth:
1379m

4.57m

Total Depth: 1940.00m

Item	Length
P.O. Sub	0.31
Double Pin	0.31
P.O. Sub	0.31
REC#126	1.50
HMV Stroke	2.18
Sampler	1.10
Telemetry Tool	6.80
Jars	2.10
Safety Joint	0.65
Pump	2.04
Screen	1.18
Valve	2.23
Deflate	0.85
Packer Stub	1.78 0.72
ASE Carrier REC#037	2.20
REC#124 Bypass Hanger	0.42
Blank Spacing Bypass Receiver	6.10 0.78
Stub	0.72
Packer Extension Sub	1.78 0.71
Drag Spring	2.08



Drill Stem Testing - Time / Pressure Listing

Company: PARAMOUNT RESOURCES LTD.
4700, 888 - 3rd Street S.W.
CALGARY, AB


Job Ticket #: D2-8621 DST#: 8
Test Date: 01/12/2001 939hrs

Well Name: PARA ET AL FORT LIARD

Contact: WILBERT CALLIHOO

Location: N-01-60-10-123-15

Chart Label	Comments	Time (Min.)	Delta P (KPag)	Pressure (KPag)	Abscissa (T+dt)/dt	Temp. (°C)	Chart Label	Comments	Time (Min.)	Delta P (KPag)	Pressure (KPag)	Abscissa (T+dt)/dt	Temp. (°C)
A	Initial Hydrostatic	0.00	0.00	16539.50		47.6			28.00	3574.20	4002.40	1.2857	48.9
B	Start of 1st Flow	0.00	0.00	406.30		47.8			29.00	3658.70	4086.90	1.2759	48.9
		1.00	45.10	451.40		47.9			30.00	3740.80	4169.00	1.2667	48.9
		2.00	31.20	437.50		48.0			31.00	3821.80	4250.00	1.2581	48.9
		3.00	21.90	428.20		48.1			32.00	3900.60	4328.80	1.2500	48.9
		4.00	8.10	414.40		48.2			33.00	3978.10	4406.30	1.2424	48.9
		5.00	10.40	416.70		48.2			34.00	4054.50	4482.70	1.2353	48.9
		6.00	20.80	427.10		48.3			35.00	4128.60	4556.80	1.2286	48.9
		7.00	19.60	425.90		48.4			36.00	4202.60	4630.80	1.2222	48.9
C	End of 1st Flow	8.00	21.90	428.20		48.5			37.00	4274.40	4702.60	1.2162	48.9
		1.00	90.30	518.50	9.0000	48.5			38.00	4345.00	4773.20	1.2105	48.9
		2.00	307.90	736.10	5.0000	48.6			39.00	4414.40	4842.60	1.2051	48.9
		3.00	509.30	937.50	3.6667	48.6			40.00	4483.90	4912.10	1.2000	48.9
		4.00	696.80	1125.00	3.0000	48.6			41.00	4551.00	4979.20	1.1951	48.9
		5.00	875.10	1303.30	2.6000	48.6			42.00	4617.00	5045.20	1.1905	48.9
		6.00	1044.00	1472.20	2.3333	48.7			43.00	4681.80	5110.00	1.1860	48.9
		7.00	1204.90	1633.10	2.1429	48.7			44.00	4746.60	5174.80	1.1818	49.0
		8.00	1358.90	1787.10	2.0000	48.7			45.00	4810.30	5238.50	1.1778	48.9
		9.00	1507.00	1935.20	1.8889	48.7			46.00	4872.80	5301.00	1.1739	49.0
		10.00	1648.20	2076.40	1.8000	48.7			47.00	4934.10	5362.30	1.1702	49.0
		11.00	1784.80	2213.00	1.7273	48.7			48.00	4994.30	5422.50	1.1667	49.0
		12.00	1916.70	2344.90	1.6667	48.8			49.00	5053.30	5481.50	1.1633	49.0
		13.00	2042.90	2471.10	1.6154	48.8			50.00	5112.40	5540.60	1.1600	49.0
		14.00	2166.70	2594.90	1.5714	48.8			51.00	5171.40	5599.60	1.1569	49.0
		15.00	2284.80	2713.00	1.5333	48.8			52.00	5228.10	5656.30	1.1538	49.0
		16.00	2401.70	2829.90	1.5000	48.8			53.00	5284.80	5713.00	1.1509	49.0
		17.00	2512.80	2941.00	1.4706	48.8			54.00	5340.40	5768.60	1.1481	49.0
		18.00	2622.80	3051.00	1.4444	48.8			55.00	5394.80	5823.00	1.1455	49.0
		19.00	2728.10	3156.30	1.4211	48.8			56.00	5449.20	5877.40	1.1429	49.0
		20.00	2832.30	3260.50	1.4000	48.8			57.00	5501.30	5929.50	1.1404	49.0
		21.00	2933.00	3361.20	1.3810	48.8			58.00	5554.50	5982.70	1.1379	49.0
		22.00	3031.30	3459.50	1.3636	48.8			59.00	5606.60	6034.80	1.1356	49.0
		23.00	3127.40	3555.60	1.3478	48.8			60.00	5657.50	6085.70	1.1333	49.0
		24.00	3220.00	3648.20	1.3333	48.8			61.00	5708.40	6136.60	1.1311	49.0
		25.00	3311.40	3739.60	1.3200	48.8			62.00	5759.40	6187.60	1.1290	49.0
		26.00	3401.70	3829.90	1.3077	48.8			63.00	5808.00	6236.20	1.1270	49.0
		27.00	3488.50	3916.70	1.2963	48.8			64.00	5857.80	6286.00	1.1250	49.1



Drill Stem Testing - Time / Pressure Listing

Company: PARAMOUNT RESOURCES LTD.
4700, 888 - 3rd Street S.W.
CALGARY, AB


Job Ticket #: D2-8621
Test Date: 01/12/2001 939hrs
DST#: 8

Well Name: PARA ET AL FORT LIARD

Contact: WILBERT CALLIHOO

Location: N-01-60-10-123-15

Chart Label	Comments	Time (Min.)	Delta P (KPag)	Pressure (KPag)	Abscissa (T+dt)/dt	Temp. (°C)	Chart Label	Comments	Time (Min.)	Delta P (KPag)	Pressure (KPag)	Abscissa (T+dt)/dt	Temp. (°C)
D	End of 1st Shutin	65.00	5864.70	6292.90	1.1231	49.1			6.00	585.70	1076.40	7.3333	49.4
E	Start of 2nd Flow	0.00	0.00	253.50		49.1			7.00	676.00	1166.70	6.4286	49.4
		1.00	71.70	325.20		49.1			8.00	763.90	1254.60	5.7500	49.4
		2.00	101.80	355.30		49.1			9.00	853.10	1343.80	5.2222	49.5
		3.00	135.40	388.90		49.1			10.00	938.70	1429.40	4.8000	49.4
		4.00	156.20	409.70		49.1			11.00	1023.20	1513.90	4.4545	49.4
		5.00	170.10	423.60		49.1			12.00	1106.50	1597.20	4.1667	49.5
		6.00	175.90	429.40		49.2			13.00	1188.70	1679.40	3.9231	49.5
		7.00	185.20	438.70		49.2			14.00	1269.70	1760.40	3.7143	49.5
		8.00	189.80	443.30		49.2			15.00	1349.60	1840.30	3.5333	49.5
		9.00	202.50	456.00		49.2			16.00	1428.30	1919.00	3.3750	49.5
		10.00	214.10	467.60		49.2			17.00	1504.70	1995.40	3.2353	49.5
		11.00	212.90	466.40		49.2			18.00	1581.10	2071.80	3.1111	49.5
		12.00	218.70	472.20		49.2			19.00	1656.30	2147.00	3.0000	49.5
		13.00	217.60	471.10		49.2			20.00	1730.40	2221.10	2.9000	49.5
		14.00	222.20	475.70		49.3			21.00	1802.20	2292.90	2.8095	49.5
		15.00	223.40	476.90		49.3			22.00	1873.90	2364.60	2.7273	49.5
		16.00	228.00	481.50		49.3			23.00	1945.70	2436.40	2.6522	49.5
		17.00	224.50	478.00		49.3			24.00	2015.10	2505.80	2.5833	49.5
		18.00	224.50	478.00		49.3			25.00	2084.60	2575.30	2.5200	49.5
		19.00	219.90	473.40		49.3			26.00	2152.80	2643.50	2.4615	49.5
		20.00	226.80	480.30		49.3			27.00	2220.00	2710.70	2.4074	49.5
		21.00	219.90	473.40		49.3			28.00	2287.10	2777.80	2.3571	49.5
		22.00	223.40	476.90		49.3			29.00	2354.20	2844.90	2.3103	49.5
		23.00	231.50	485.00		49.3			30.00	2420.20	2910.90	2.2667	49.5
		24.00	229.10	482.60		49.3			31.00	2485.00	2975.70	2.2258	49.5
		25.00	228.00	481.50		49.3			32.00	2548.70	3039.40	2.1875	49.5
		26.00	224.50	478.00		49.4			33.00	2612.30	3103.00	2.1515	49.6
		27.00	229.10	482.60		49.4			34.00	2674.80	3165.50	2.1176	49.5
		28.00	233.80	487.30		49.4			35.00	2736.20	3226.90	2.0857	49.5
		29.00	223.40	476.90		49.4			36.00	2798.70	3289.40	2.0556	49.6
F	End of 2nd Flow	30.00	237.20	490.70		49.4			37.00	2860.00	3350.70	2.0270	49.6
		1.00	110.00	600.70	39.0000	49.4			38.00	2920.20	3410.90	2.0000	49.6
		2.00	209.50	700.20	20.0000	49.4			39.00	2979.20	3469.90	1.9744	49.6
		3.00	306.80	797.50	13.6667	49.4			40.00	3038.30	3529.00	1.9500	49.6
		4.00	400.50	891.20	10.5000	49.4			41.00	3096.10	3586.80	1.9268	49.6
		5.00	494.30	985.00	8.6000	49.4			42.00	3154.00	3644.70	1.9048	49.6



Drill Stem Testing - Time / Pressure Listing

Company: PARAMOUNT RESOURCES LTD.
4700, 888 - 3rd Street S.W.
CALGARY, AB

Job Ticket #: D2-8621

DST#: 8


Test Date: 01/12/2001 939hrs

Well Name: PARA ET AL FORT LIARD

Contact: WILBERT CALLIHOO

Location: N-01-60-10-123-15

Chart Label	Comments	Time (Min.)	Delta P (KPag)	Pressure (KPag)	Abscissa (T+dt)/dt	Temp. (°C)	Chart Label	Comments	Time (Min.)	Delta P (KPag)	Pressure (KPag)	Abscissa (T+dt)/dt	Temp. (°C)
		43.00	3210.70	3701.40	1.8837	49.6			80.00	4972.30	5463.00	1.4750	49.7
		44.00	3268.60	3759.30	1.8636	49.6			81.00	5011.70	5502.40	1.4691	49.7
		45.00	3323.00	3813.70	1.8444	49.6			82.00	5051.00	5541.70	1.4634	49.7
		46.00	3378.60	3869.30	1.8261	49.6			83.00	5090.40	5581.10	1.4578	49.7
		47.00	3433.00	3923.70	1.8085	49.6			84.00	5128.60	5619.30	1.4524	49.8
		48.00	3487.40	3978.10	1.7917	49.6			85.00	5166.80	5657.50	1.4471	49.7
		49.00	3540.60	4031.30	1.7755	49.6			86.00	5205.00	5695.70	1.4419	49.7
		50.00	3595.00	4085.70	1.7600	49.6			87.00	5243.20	5733.90	1.4368	49.8
		51.00	3647.10	4137.80	1.7451	49.6			88.00	5281.40	5772.10	1.4318	49.8
		52.00	3699.20	4189.90	1.7308	49.6			89.00	5318.40	5809.10	1.4270	49.8
		53.00	3750.10	4240.80	1.7170	49.6			90.00	5355.40	5846.10	1.4222	49.8
		54.00	3801.00	4291.70	1.7037	49.6			91.00	5392.50	5883.20	1.4176	49.8
		55.00	3851.90	4342.60	1.6909	49.6			92.00	5429.50	5920.20	1.4130	49.8
		56.00	3901.70	4392.40	1.6786	49.6			93.00	5465.40	5956.10	1.4086	49.8
		57.00	3951.50	4442.20	1.6667	49.6			94.00	5501.30	5992.00	1.4043	49.8
		58.00	4000.10	4490.80	1.6552	49.6			95.00	5536.00	6026.70	1.4000	49.8
		59.00	4048.70	4539.40	1.6441	49.7			96.00	5571.90	6062.60	1.3958	49.8
		60.00	4096.20	4586.90	1.6333	49.6			97.00	5606.60	6097.30	1.3918	49.8
		61.00	4144.80	4635.50	1.6230	49.6			98.00	5642.50	6133.20	1.3878	49.8
		62.00	4191.10	4681.80	1.6129	49.7			99.00	5677.20	6167.90	1.3838	49.8
		63.00	4237.40	4728.10	1.6032	49.6			100.00	5710.80	6201.50	1.3800	49.8
		64.00	4283.70	4774.40	1.5938	49.7			101.00	5745.50	6236.20	1.3762	49.8
		65.00	4330.00	4820.70	1.5846	49.7			102.00	5779.10	6269.80	1.3725	49.8
		66.00	4375.10	4865.80	1.5758	49.7			103.00	5812.60	6303.30	1.3689	49.8
		67.00	4421.40	4912.10	1.5672	49.7			104.00	5846.20	6336.90	1.3654	49.8
		68.00	4465.40	4956.10	1.5588	49.7			105.00	5878.60	6369.30	1.3619	49.8
		69.00	4509.40	5000.10	1.5507	49.7			106.00	5911.00	6401.70	1.3585	49.8
		70.00	4553.30	5044.00	1.5429	49.7			107.00	5944.60	6435.30	1.3551	49.8
		71.00	4597.30	5088.00	1.5352	49.7			108.00	5977.00	6467.70	1.3519	49.8
		72.00	4640.10	5130.80	1.5278	49.7			109.00	6008.20	6498.90	1.3486	49.8
		73.00	4683.00	5173.70	1.5205	49.7			110.00	6040.60	6531.30	1.3455	49.9
		74.00	4724.60	5215.30	1.5135	49.7			111.00	6071.90	6562.60	1.3423	49.9
		75.00	4766.30	5257.00	1.5067	49.7			112.00	6103.10	6593.80	1.3393	49.9
		76.00	4808.00	5298.70	1.5000	49.7			113.00	6134.40	6625.10	1.3363	49.9
		77.00	4849.60	5340.30	1.4935	49.7			114.00	6165.60	6656.30	1.3333	49.9
		78.00	4890.20	5380.90	1.4872	49.7			115.00	6196.90	6687.60	1.3304	49.9
		79.00	4930.70	5421.40	1.4810	49.7			116.00	6227.00	6717.70	1.3276	49.9



Drill Stem Testing - Time / Pressure Listing

Company: PARAMOUNT RESOURCES LTD.
4700, 888 - 3rd Street S.W.
CALGARY, AB


Job Ticket #: D2-8621 DST#: 8
Test Date: 01/12/2001 939hrs

Well Name: PARA ET AL FORT LIARD

Contact: WILBERT CALLIHO

Location: N-01-60-10-123-15

Chart Label	Comments	Time (Min.)	Delta P (KPag)	Pressure (KPag)	Abscissa (T+dt)/dt	Temp. (°C)	Chart Label	Comments	Time (Min.)	Delta P (KPag)	Pressure (KPag)	Abscissa (T+dt)/dt	Temp. (°C)
		117.00	6258.20	6748.90	1.3248	49.9			154.00	7225.80	7716.50	1.2468	50.0
		118.00	6287.20	6777.90	1.3220	49.9			155.00	7249.00	7739.70	1.2452	50.1
		119.00	6317.30	6808.00	1.3193	49.9			156.00	7272.10	7762.80	1.2436	50.0
		120.00	6347.30	6838.00	1.3167	49.9			157.00	7296.40	7787.10	1.2420	50.0
		121.00	6376.30	6867.00	1.3140	49.9			158.00	7319.60	7810.30	1.2405	50.1
		122.00	6408.70	6899.40	1.3115	49.9			159.00	7342.70	7833.40	1.2390	50.1
		123.00	6437.60	6928.30	1.3089	49.9			160.00	7365.90	7856.60	1.2375	50.1
		124.00	6466.60	6957.30	1.3065	49.9			161.00	7389.00	7879.70	1.2360	50.1
		125.00	6495.50	6986.20	1.3040	49.9			162.00	7412.20	7902.90	1.2346	50.1
		126.00	6495.50	6986.20	1.3016	50.0			163.00	7434.20	7924.90	1.2331	50.1
		127.00	6552.20	7042.90	1.2992	49.9			164.00	7456.20	7946.90	1.2317	50.1
		128.00	6553.40	7044.10	1.2969	50.0			165.00	7479.30	7970.00	1.2303	50.1
		129.00	6608.90	7099.60	1.2946	49.9			166.00	7501.30	7992.00	1.2289	50.1
		130.00	6610.10	7100.80	1.2923	50.0			167.00	7523.30	8014.00	1.2275	50.1
		131.00	6636.70	7127.40	1.2901	50.0			168.00	7545.30	8036.00	1.2262	50.1
		132.00	6663.30	7154.00	1.2879	50.0			169.00	7567.30	8058.00	1.2249	50.1
		133.00	6691.10	7181.80	1.2857	50.0			170.00	7589.30	8080.00	1.2235	50.1
		134.00	6718.90	7209.60	1.2836	50.0			171.00	7610.10	8100.80	1.2222	50.1
		135.00	6745.50	7236.20	1.2815	50.0			172.00	7632.10	8122.80	1.2209	50.1
		136.00	6772.10	7262.80	1.2794	50.0			173.00	7652.90	8143.60	1.2197	50.1
		137.00	6798.70	7289.40	1.2774	50.0			174.00	7674.90	8165.60	1.2184	50.1
		138.00	6825.40	7316.10	1.2754	50.0			175.00	7695.70	8186.40	1.2171	50.1
		139.00	6852.00	7342.70	1.2734	50.0			176.00	7716.60	8207.30	1.2159	50.1
		140.00	6877.40	7368.10	1.2714	50.0			177.00	7737.40	8228.10	1.2147	50.1
		141.00	6902.90	7393.60	1.2695	50.0			178.00	7758.20	8248.90	1.2135	50.1
		142.00	6929.50	7420.20	1.2676	50.0			179.00	7779.10	8269.80	1.2123	50.1
		143.00	6955.00	7445.70	1.2657	50.0			180.00	7799.90	8290.60	1.2111	50.1
		144.00	6979.30	7470.00	1.2639	50.0			181.00	7819.60	8310.30	1.2099	50.1
		145.00	7005.90	7496.60	1.2621	50.0			182.00	7840.40	8331.10	1.2088	50.2
		146.00	7030.20	7520.90	1.2603	50.0			183.00	7860.10	8350.80	1.2077	50.1
		147.00	7054.50	7545.20	1.2585	50.0			184.00	7880.90	8371.60	1.2065	50.2
		148.00	7080.00	7570.70	1.2568	50.0			185.00	7900.60	8391.30	1.2054	50.2
		149.00	7104.30	7595.00	1.2550	50.0			186.00	7920.30	8411.00	1.2043	50.2
		150.00	7128.60	7619.30	1.2533	50.0			187.00	7940.00	8430.70	1.2032	50.2
		151.00	7152.90	7643.60	1.2517	50.0			188.00	7959.60	8450.30	1.2021	50.2
		152.00	7177.20	7667.90	1.2500	50.0			189.00	7979.30	8470.00	1.2011	50.2
		153.00	7201.50	7692.20	1.2484	50.0			190.00	7999.00	8489.70	1.2000	50.2



Drill Stem Testing - Time / Pressure Listing

Company: PARAMOUNT RESOURCES LTD.
4700, 888 - 3rd Street S.W.
CALGARY, AB

Job Ticket #: D2-8621 DST#: 8
Test Date: 01/12/2001 939hrs

Well Name: PARA ET AL FORT LIARD


Contact: WILBERT CALLIHOO


Location: N-01-60-10-123-15

Chart Label	Comments	Time (Min.)	Delta P (KPag)	Pressure (KPag)	Abscissa (T+dt)/dt	Temp. (°C)
G	End of 2nd Shutin	191.00	8018.70	8509.40	1.1990	50.2
Q	Final Hydrostatic	0.00	0.00	16197.00		50.4



Homer Plot
PARA ET AL FORT LIARD (N-01-60-10-123-15) DST#8 OUTSIDE Rec#124
Shut-in# 1

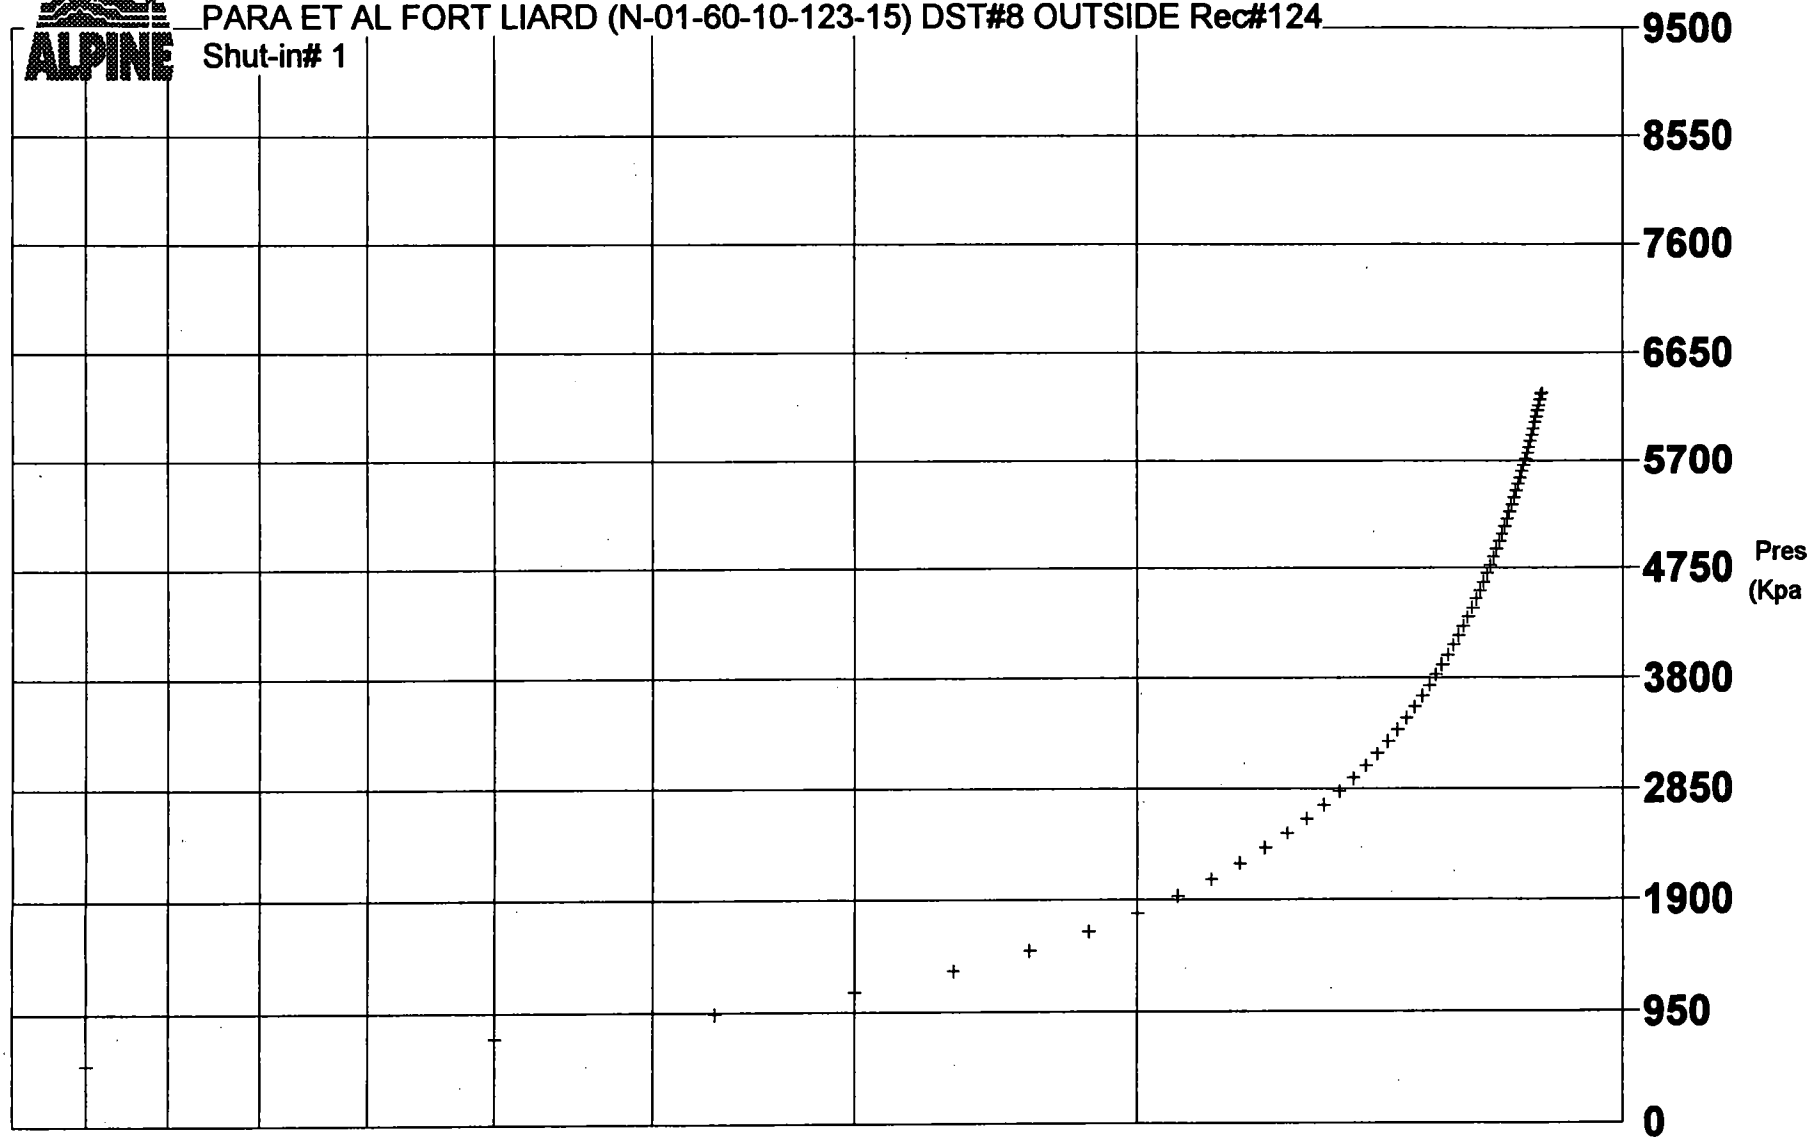






Time/Pressure Plot

PARA ET AL FORT LIARD (N-01-60-10-123-15) DST#8 FLUID Rec#126

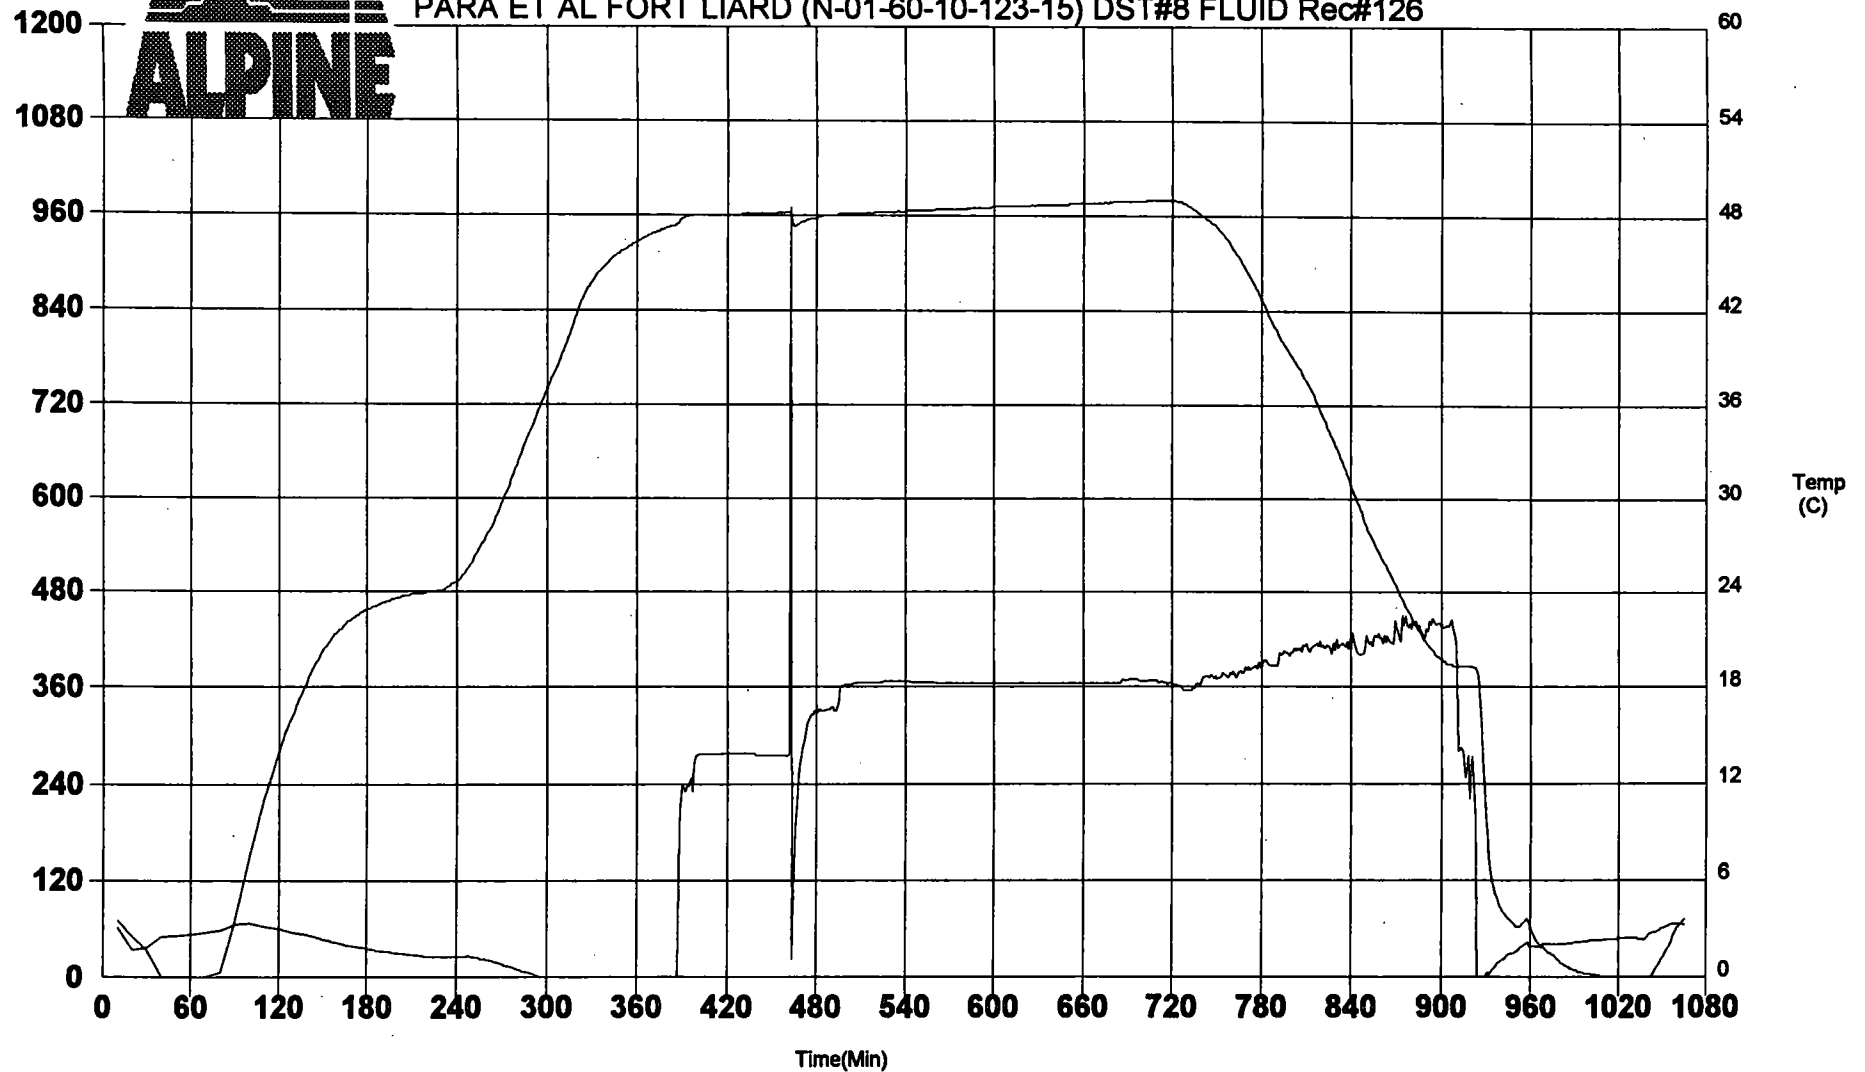

A Initial Hydrostatic - 0
B Start of 1st Flow - 0
C End of 1st Flow - 230
D End of 1st Shutin - 276
E Start of 2nd Flow - 22

F End of 2nd Flow - 333
G End of 2nd Shutin - 365
Q Final Hydrostatic - 365



Time/Pressure Plot

PARA ET AL FORT LIARD (N-01-60-10-123-15) DST#8 OUTSIDE Rec#037



A Initial Hydrostatic - 16593
B Start of 1st Flow - 368
C End of 1st Flow - 372
D End of 1st Shutin - 6289
E Start of 2nd Flow - 183

F End of 2nd Flow - 419
G End of 2nd Shutin - 8493
Q Final Hydrostatic - 15949



Time/Pressure Plot

PARA ET AL FORT LIARD (N-01-60-10-123-15) DST#8 OUTSIDE Rec#124



A Initial Hydrostatic - 16540
B Start of 1st Flow - 406
C End of 1st Flow - 428
D End of 1st Shutin - 6293
E Start of 2nd Flow - 254

F End of 2nd Flow - 491
G End of 2nd Shutin - 8509
Q Final Hydrostatic - 16197
