


Downhole Schematic

ANADARKO ARROWHEAD RIVER F-56

Bottom Hole Location 300/F-56-06.04-001.22/00	Surface Legal Location	License # NT001978	Field Name FT LIARD	Province NORTHWEST TERRITORIES	
Well Profile	Fluid Type	Original KB Elevation (m)	KB-Ground Distance (m)	KB-Casing Flange Distance (m)	KB-Tubing Head Distance (m)

Directions To Well

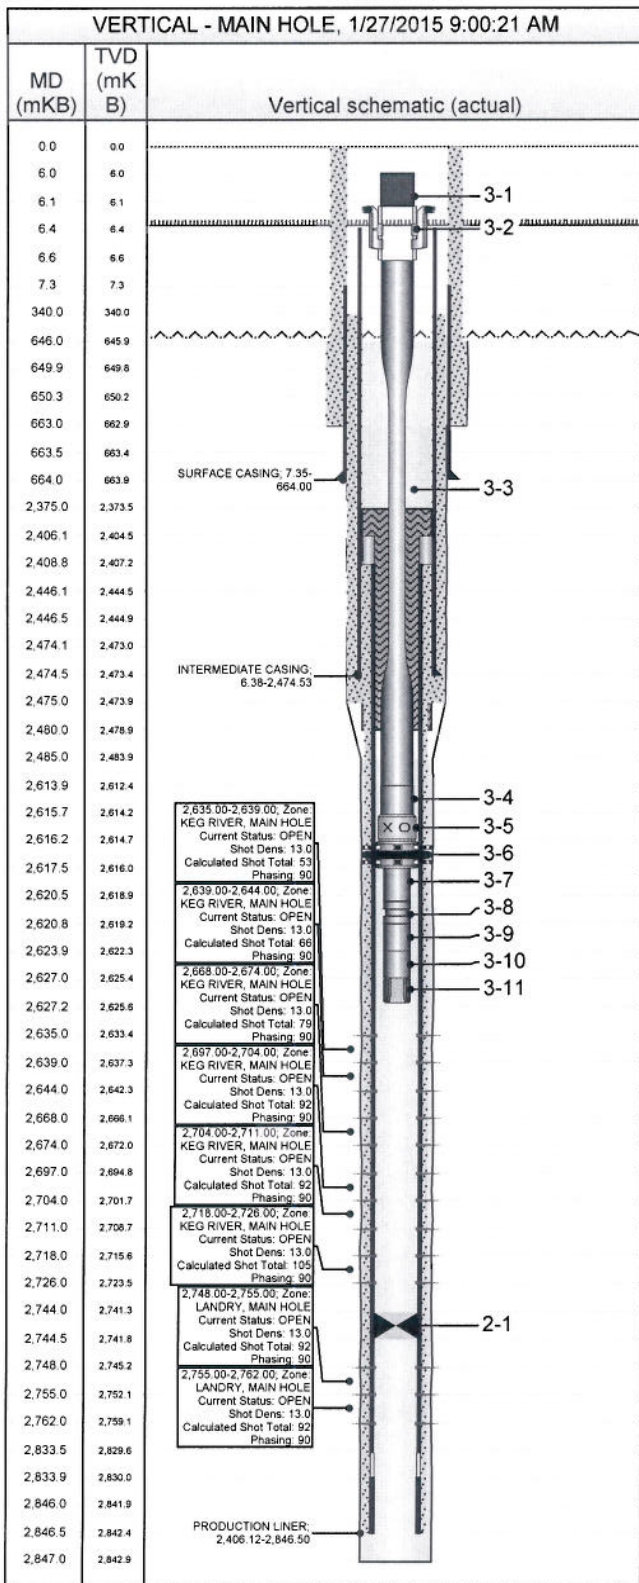

Plug Back Total Depths

Date	Depth (mKB)

Casing Strings

Csg Des	OD (mm)	Wt/Len (kg/m)	Grade	Set Depth (MD) (mKB)
SURFACE CASING	244.5	59.530	L-80	663.00
SURFACE CASING	244.5	59.530	L80	664.00
INTERMEDIATE CASING	177.8	38.690	L80	2,474.53
INTERMEDIATE CASING	177.8	38.690	L-80	2,475.00
PRODUCTION LINER	114.3	17.260	L80	2,846.50

Cement Stages

Des	Type	Top (mKB)	Btm (mKB)	Rtns Mix (%)	Rtns Displ. (%)	Vol Cement Ret (m³)
SURFACE CASING	Casing	0.00	663.00	400	100	4.00
INTERMEDIATE CASING	Casing	340.00	2,474.50	400	100	
	Plug	2,375.00	2,480.00			
PRODUCTION LINER	Casing	2,406.12	2,846.50	800	1,500	

Perforations

Zone	Top (mKB)	Btm (mKB)	Current Status
KEG RIVER, MAIN HOLE	2,635.00	2,639.00	OPEN
KEG RIVER, MAIN HOLE	2,639.00	2,644.00	OPEN
KEG RIVER, MAIN HOLE	2,668.00	2,674.00	OPEN
KEG RIVER, MAIN HOLE	2,697.00	2,704.00	OPEN
KEG RIVER, MAIN HOLE	2,704.00	2,711.00	OPEN
KEG RIVER, MAIN HOLE	2,718.00	2,726.00	OPEN
LANDRY, MAIN HOLE	2,748.00	2,755.00	OPEN
LANDRY, MAIN HOLE	2,755.00	2,762.00	OPEN

Tubing Strings

PACKER ASSEMBLY set at 2,627.16mKB on 3/17/2004 00:00

Tubing Description	String Max N...	Wt (kg/m)	String Grade	Set Depth (mKB)
PACKER ASSEMBLY	73.0			2,627.16

Comment

Item #	Jts	Item Des	OD (mm)	ID (mm)	Len (m)	Top (mKB)	Btm (mKB)
3-1	1	DOGNUT	73.0		0.15	6.00	6.15
3-2	0	TUBING HANGER AND CHANGE OVER	88.9		0.49	6.15	6.64
3-3	0	274 JOINTS OF 73 MM EUE TUBING	73.0		2,607.22	6.64	2,613.86
3-4	0	73 MM EUE HANDLING PUP	73.0		1.87	2,613.86	2,615.73
3-5	0	X/O TO 60.3 MM COATED ON-OFF W/1.87" X PROFILE	88.9		0.49	2,615.73	2,616.22
3-6	0	WEATHERFORD 60.3 X 114 MM COATED QDG PACKER	101.6		1.28	2,616.22	2,617.50
3-7	0	COATED 60.3 MM PUP JOINT	60.3		3.04	2,617.50	2,620.54
