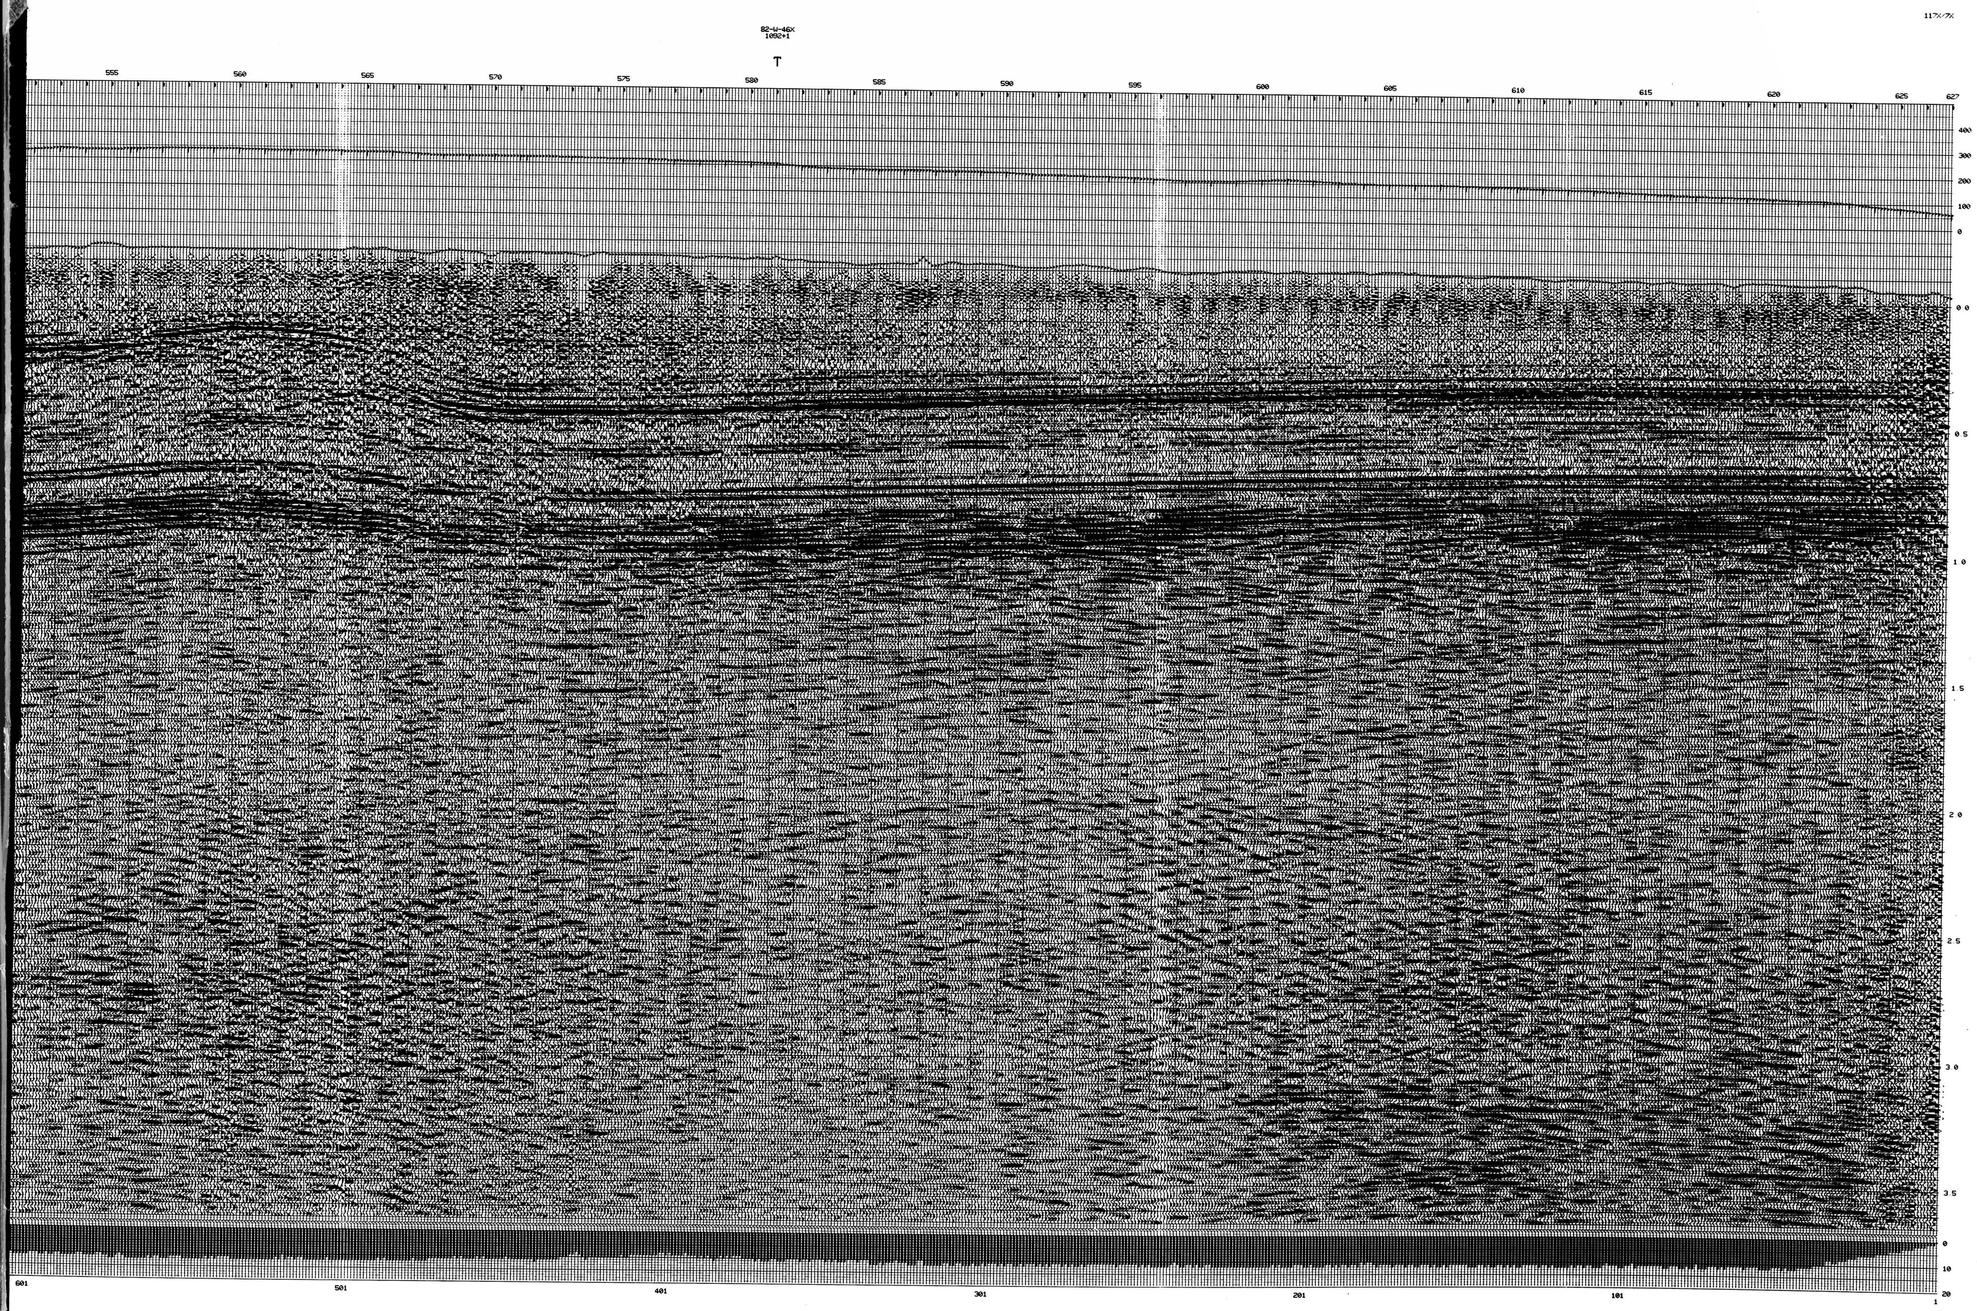

24 6-06-05-115

GEO-X SYSTEMS LTD.
CALGARY ALBERTA

FLAG

LINE: 82-W-117X/7X TYPE: S-RP
DIRECTION ⟶ N.E.
PROJECT: SAMMON'S CREEK
LOCATION: DISTRICT OF MACKENZIE NTS 96H/106H
CLIENT: PETRO-CANADA EXPLORATION INC.

SURFACE ELEVATIONS

SHOT BY WESTERN GEOPHYSICAL, PTY. 362 DATE 3/82

SPREAD 1584 m - 33m. x 33m. - 1584 m.
SOURCE 2 kg at 18 m
RECEIVERS GEOSPACE 20D, 10 Hz, 9 OVER 53 m
SOURCE INTERVAL 132 m GROUP INTERVAL 33 m

SURFACE IN TIME

AMPLIFIERS DFS V FIELD FILTER 8-128 Hz NOTCH OUT
GAIN MODE IFP TAPE FORMAT SEG B

PROCESSED AT GEO-X DATE 6/82

1 DIGITAL CONVERSION SAMPLE RATE 2 ms
2 AMPLITUDE RECOVERY At^2

PREFILTER

3 DECONVOLUTION TYPE SPIKING
OPERATOR LENGTH 60 ms. PREWHITENING 1%
DESIGN GATE 400-2400 ms. SLOPING
4 STRUCTURAL CORRECTIONS
DATUM SEA LEVEL DATUM VELOCITY 3506 m/sec
PROCESSING DATUM -250 m.
(X) ELEVATIONS (X) WEATHERING (X) DRIFT
10 ANALYSIS STATISTICAL SURFACE CONSISTENT STATICS
5 11 MOVEOUT (5) PRELIMINARY (11) FINAL
6 SCALING
7 12 STATICS (7) SURFACE STACK RESIDUAL
(12) CROSS CORRELATION
( )
8 WORK SECTION DISPLAY
9 TRACE KILLS
13 MUTE DISTANCE (m) 314 924 3168
TIME (ms.) 300 550-650 1700
14 GATHER FOLD 12
15 STACK STACK REEL
16 FILTER (16) 12/16-80/90 Hz, 0-2500 ms
( ) 12/16-50/60 Hz, 2500-4000 ms
( )
17 ADDITIONAL PROCESSING
(17) LINEAR RAMP SCALING
TIME 0-130, 250-1600, 2300, 3000-4000
%SCALER 70, 100, 120, 150
18 EQUALIZATION 400-2400ms

76407

Geoex Ltd.
2060 Holiday Rd.
Ottawa, Ont.
Canada K1G 3C5
Tel. (613) 731-9671
Telex: 053-3502
Cable: TERRA

PROJ. NO. 2 0 0 0 0 0 1 8

LINE NO. 8 2 - W - 1 1 7 X

PART NO. 1 OF 2

R.R. 8X

terra surveys ltd
2060 Walkley Rd. Ottawa, Ont.
Canada K1G 3P5
Tel. (613) 731-9571
Telex: 053-3502 Cable: TERRA
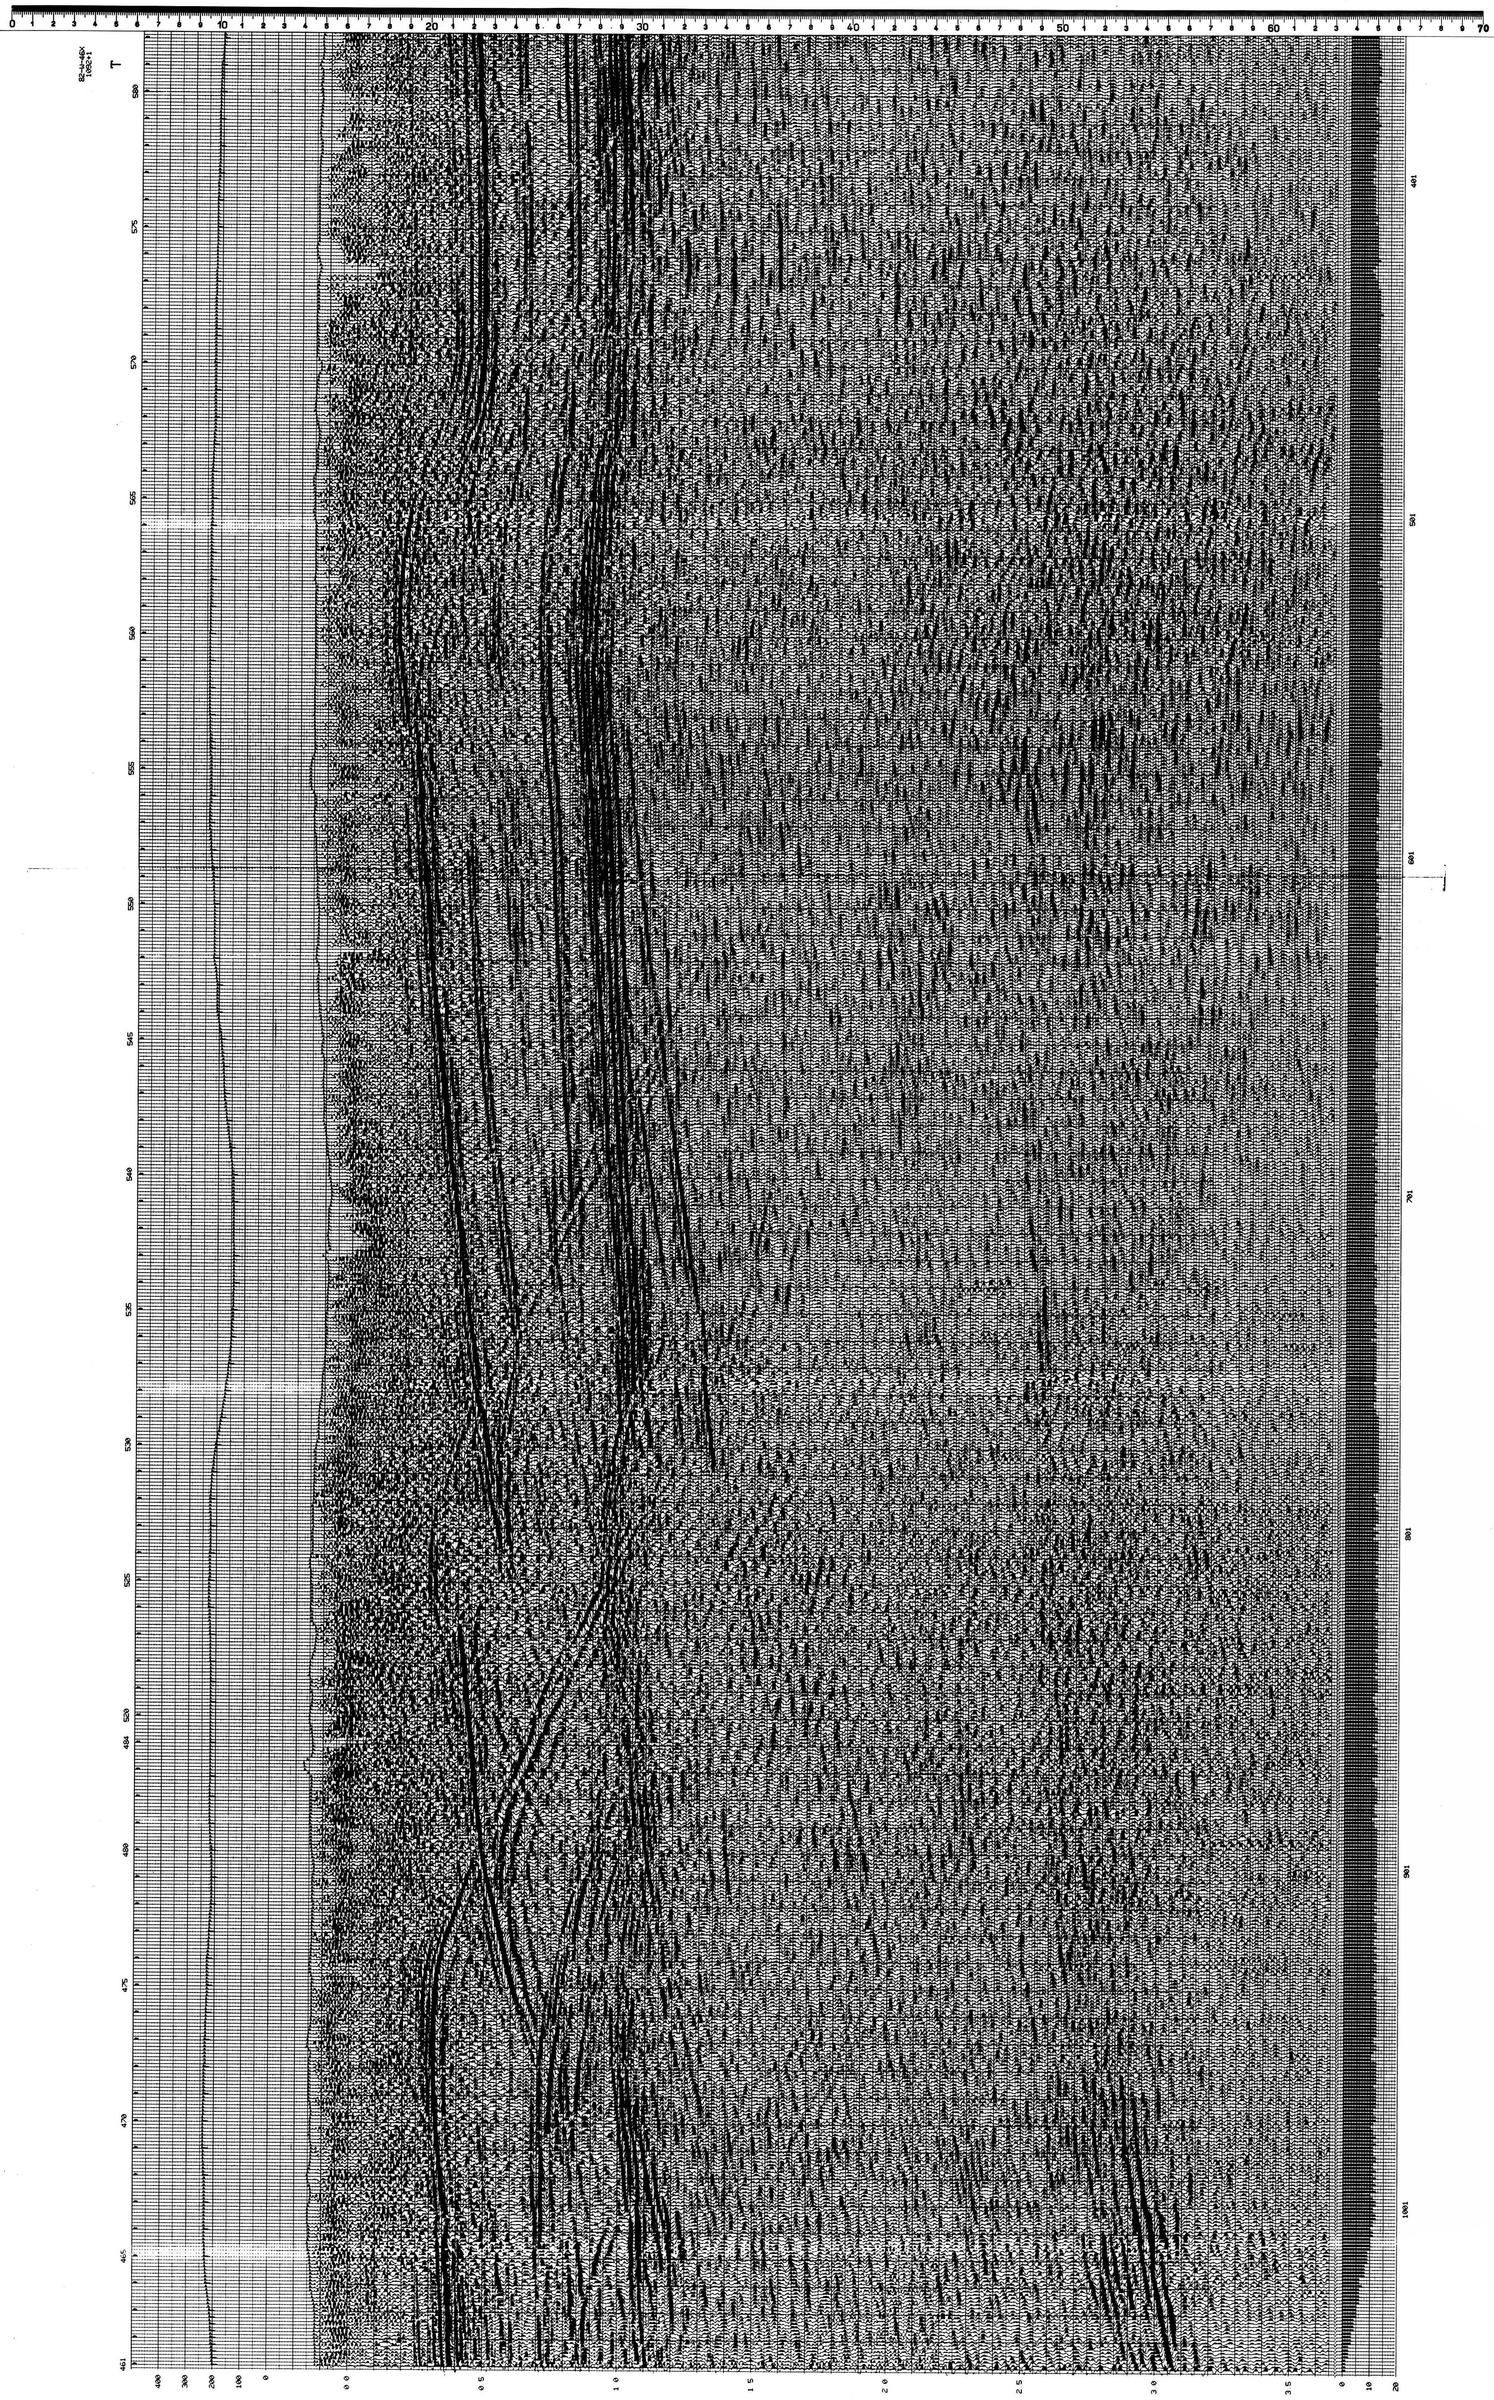
PROJ. NO. 2 4 6 - 0 6 - 0 5 - 1 1 5 LINE NO. 8 2 - W - 1 1 7 X PART NO. 2 OF 2 R.R. 8X
